



City of Redlands: Municipal Utilities & Engineering Department  
35 Cajon Street, Suite 15A. Redlands, CA 92373  
(909) 798-7698

## PMP 2023 Street Resurfacing Project

**City Engineer: Goutam Dobey**  
**Phone:** (909) 435-7431 (Cell)  
**Email:** gdobey@cityofredlands.org

**City Inspector: Daniel Murbarger**  
**Phone:** (909) 437-8440 (Cell)  
**Email:** dmurbarger@cityofredlands.org

### PROJECT DETAILS

**Contractor:** Matich Corporation


**Description:** This project will replace approximately twenty-five (25) lane miles of streets, selective replacement of curb and gutter, and striping replacement at various locations throughout the City.

**Start Date:** 02/20/2024

**Anticipated End Date:** June 2024

**Work Schedule:** M-F (7am - 4PM) excluding City recognized holidays.

### CONSTRUCTION PROGRESS

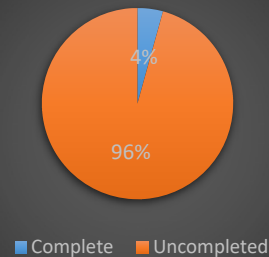

### Project Updates & Issues

The Contractor began replacing concrete curb and gutter on Herald St., Oxford Dr., Church St., and Alta Street. Potholing began on Sophia Ct., Buckingham Dr. and Michael Ct. Construction notices have been given to affected residents. If restricted parking is necessary, "No Parking" signs will be posted 48 hours in advance of construction activities.

### 2 Week Look Ahead

The Contractor will continue to replace concrete curb and gutter, and potholing in various locations in the City.

### Current Construction Process

The Contractor is currently on schedule with replacing concrete curb and gutter, and potholing in various locations in the City.



Curb and Gutter Replacement

### BUDGET TRACKING

Project Cost:	\$	4,381,606.00
Approved Change Orders	\$	-
Total Contract Value	\$	4,381,606.00
Expended to Date:		
Balance:	\$	4,381,606.00

### ADDITIONAL INFORMATION

Register for the distribution list to receive regular updates by sending an email to:  
[MUEDProjectUpdate@cityofredlands.org](mailto:MUEDProjectUpdate@cityofredlands.org)

INTERACTIVE CITY CAPITAL IMPROVEMENT PROJECT MAP LINK:

<https://www.cityofredlands.org/node/3710>
