



City of Redlands: Municipal Utilities & Engineering Department
 35 Cajon Street, Suite 15A, Redlands, CA 92373
 (909) 798-7698

2023 Citywide Sidewalk and ADA Ramp Replacement Project

City Engineer: Goutam Dobey
Phone: (909) 435-7431 (Cell)
Email: gdobey@cityofredlands.org

City Inspector: James Peters
Phone: (909) 518-4552 (Cell)
Email: jpeters@cityofredlands.org

PROJECT DETAILS


Contractor: Tryco General Engineering

Description: This Project will replace sidewalk and curb ramps at various locations throughout the City.

Start Date: 03/04/2024
Anticipated End Date: June 2024

Work Schedule: M-F (7am - 4pm) excluding City recognized holidays.

CONSTRUCTION PROGRESS

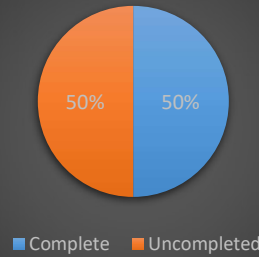

Project Updates & Issues

The contractor is resuming work in Area B. They are currently demoing sidewalks and drive approaches on Dracena Ct. They are also grading and compacting on Evergreen Ct. in preparation for concrete placement. Additionally, they are completing the concrete placement for ADA ramps and sidewalks at Cimarron Ct.

2-Week Look Ahead

The contractor will commence with demolition, form setting, and concrete pouring for new ADA ramps and sidewalks along Cimarron Ct, Cimarron Dr, Birch Ct, and Dracena Ct. This phase is anticipated to conclude by May 17th. Subsequently, attention will shift to Area A, encompassing Clark St, Grant St, Cajon St, and Nordina St.

Current Construction Process

Construction notices have been given to affected residents. If restricted parking is necessary, "No Parking" signs will be posted 48 hours in advance of construction activities.



Demoing sidewalks on Dracena Ct.

BUDGET TRACKING

Project Cost:	\$	1,000,000.00
Approved Change Orders	\$	-
Total Contract Value	\$	1,000,000.00
Expended to Date:	\$	568,377.00
Balance:	\$	431,623.00

ADDITIONAL INFORMATION

Register for the distribution list to receive regular updates by sending an email to:
MUEDProjectUpdate@cityofredlands.org

INTERACTIVE CITY CAPITAL IMPROVEMENT PROJECT MAP LINK:

<https://www.cityofredlands.org/node/3710>
