



**City of Redlands: Municipal Utilities & Engineering Department**  
 35 Cajon Street, Suite 15A, Redland, CA 92373  
 (909) 798-7698

## 2023 ALLEY PAVING IMPROVEMENT PROJECT


**City Engineer: Goutam Dobey**  
 Phone: (909) 435-7431 (Cell)  
 Email: gdobey@cityofredlands.org

**City Inspector: Jim Peters**  
 Phone: (909) 518-4552 (Cell)  
 Email: jpeters@cityofredlands.org

### PROJECT DETAILS

**Contractor:** TRYCO GENERAL ENGINEERING  
**Description:** This project will involve repaving 14 existing alleys and installing a ribbon gutter to aid in drainage at various locations throughout the City.  
**Start Date:** 04/08/2024  
**Anticipated End Date:** AUGUST 2024  
**Work Schedule:** M-F (7am - 4PM) excluding city recognized holidays.

### CONSTRUCTION PROGRESS

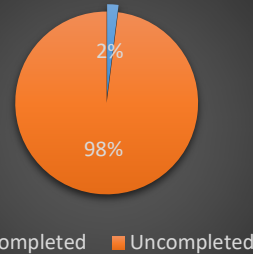

### Project Updates & Issues


**This week the contractor is conducting grinding work on the existing Alley #4 west of Buena Vista Street, between Olive Ave. and Glenwood Dr. in preparation for the installation of a storm drain system. Additionally, they are grinding the existing pavement on Alley #5 east of Buena Vista Street between Olive Ave. and Glenwood Dr. for repaving purposes and the installation of a ribbon gutter.**

### 2-Week Look Ahead

**The Contractor will be demoing, grading, and repaving Alley #4 and Alley #5, east and west of Buena Vista Street between Olive Avenue and Glenwood Drive.**

### Current Construction Process

**Construction notices have been given to affected residents. If restricted parking is necessary, "No Parking" signs will be posted 48 hours in advance of construction activities. Alleys will be closed for 3 weeks.**

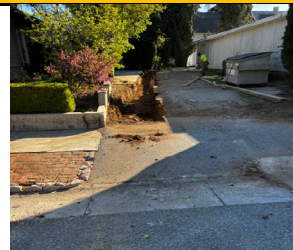

**Alley 5 setting forms for ribbon gutter**

### BUDGET TRACKING

|                             |           |                     |
|-----------------------------|-----------|---------------------|
| Project Cost:               | \$        | 1,738,285.00        |
| Approved Change Orders      | \$        | -                   |
| <b>Total Contract Value</b> | <b>\$</b> | <b>1,738,285.00</b> |
| Expended to Date:           | \$        | -                   |
| Balance:                    | \$        | 1,738,285.00        |

### ADDITIONAL INFORMATION

**Register online to receive weekly updates by sending an email with the subject line: 2023 Alley Project Updates.**  
**To: [MUEDProjectUpdate@cityofredlands.org](mailto:MUEDProjectUpdate@cityofredlands.org)**

INTERACTIVE CITY CAPITAL IMPROVEMENT PROJECT MAP LINK:

<https://www.cityofredlands.org/node/3710>
